

# CONSTRUCTION STATUS REPORT

2023 Street Improvements Project  
Loretto, Minnesota

## STATUS REPORT NO. 1

May 10, 2024

This report will provide an update on the construction status of the 2023 Street Improvements Project and the events that have transpired to date.

### **WORK COMPLETED TO DATE BY Omann Brothers Paving:**

- Temporary Mailboxes installed (see figure below for location)

### **WORK COMPLETED FOR THE WEEK BEGINNING May 6 through May 10, 2024**


- Milled off top layer of pavement.
- Tree and fence removals

### **WORK SCHEDULED FOR THE WEEK BEGINNING May 13, 2024**

- Removal of remaining pavement layers scheduled for May 13<sup>th</sup> and 14<sup>th</sup>
- Driveway removals scheduled for May 13<sup>th</sup> and 14<sup>th</sup>
- Storm Sewer installation on the southern portion of Meadow Drive scheduled to start May 15<sup>th</sup>

**\*\*SCHEDULE DEPENDENT WEATHER PERMITTING\*\***

Notes compiled by Joe Elsenpeter

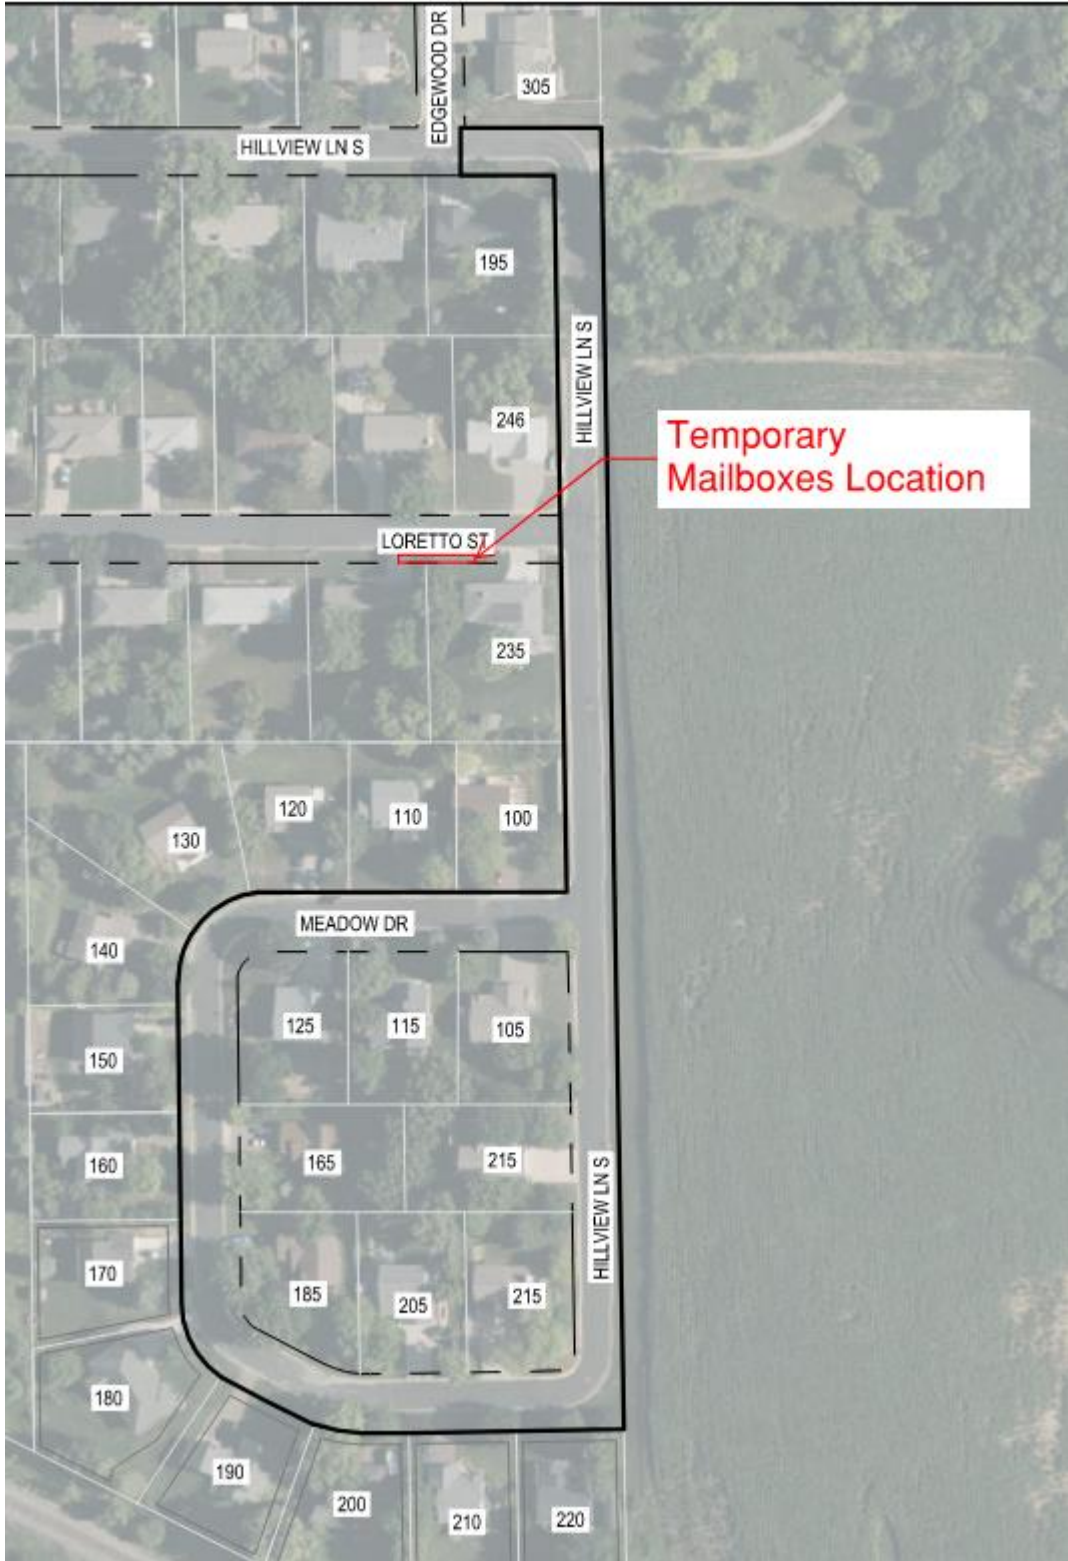

Temporary  
Mailboxes Location
