

CONSTRUCTION STATUS REPORT

2023 Street Improvements Project
Loretto, Minnesota

STATUS REPORT NO. 6

June 14th, 2024

This report will provide an update on the construction status of the 2023 Street Improvements Project and the events that have transpired to date.

WORK COMPLETED TO DATE BY Omann Brothers Paving:

- Temporary Mailboxes installed
- Milled off pavement for the project area

WORK COMPLETED FOR THE WEEK BEGINNING June 10 through June 14, 2024

- The majority of the storm sewer along the southern and western portions of Meadow Drive has been installed, the remaining storm sewer will be installed in the coming weeks
- Restoration for all storm sewer in the green spaces will be completed at a later date

WORK SCHEDULED FOR THE WEEK BEGINNING June 17, 2024

- The placement of sand, gravel, and drain tile will continue in the southern portion of Meadow Drive, see the figure below.
- While sand and gravel is being placed, portions of the road will be closed, residents in the affected areas will be notified in advance
- Work on installing a sump line along the northern portion of Meadow Drive


****SCHEDULE DEPENDENT WEATHER PERMITTING****

For questions or concerns about the project, please contact the following:

Field Engineer:
Joe Elsenpeter
(612)-477-1120
Joe.Elsenpeter@stantec.com

Project Engineer:
Nick Wyers
(952)-838-5661
Nick.Wyers@stantec.com

Notes compiled by Joe Elsenpeter

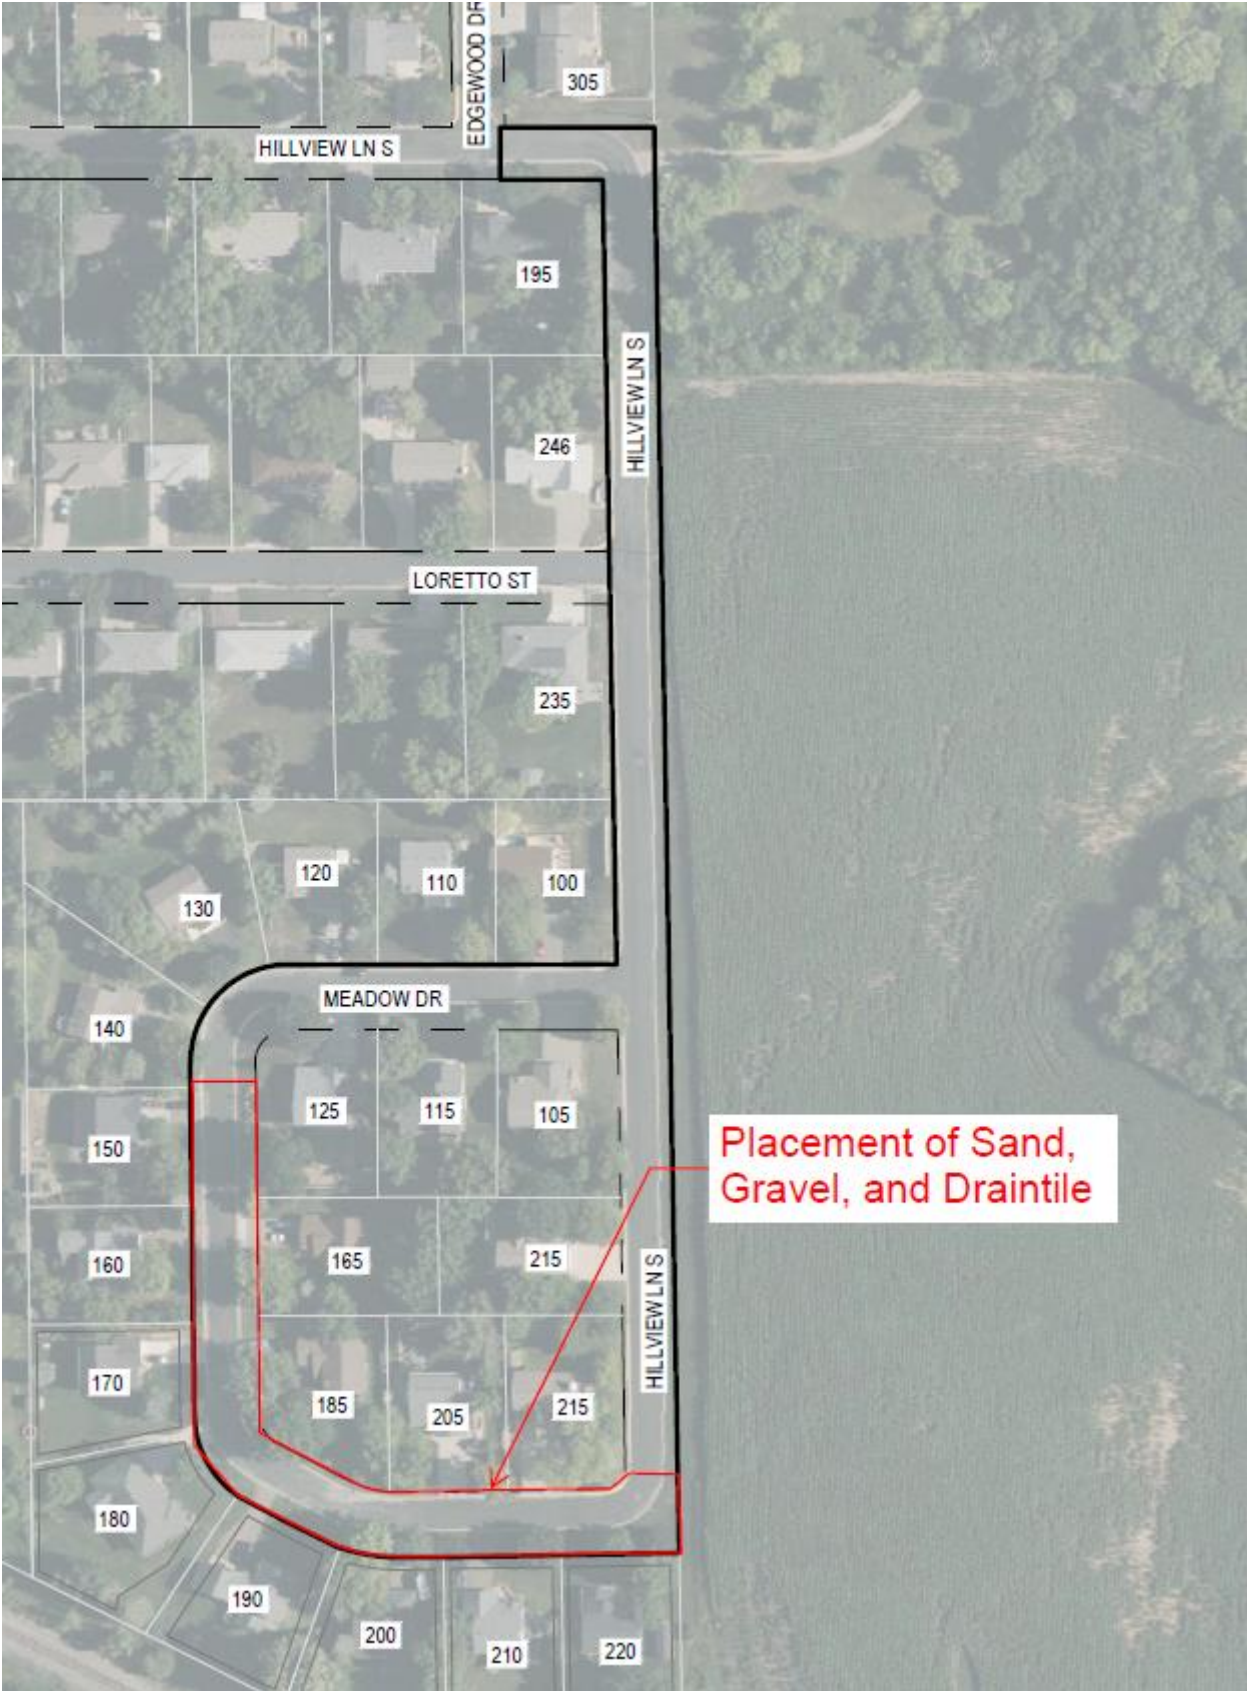

HILLVIEW LN S

EDGEWOOD DR

305

195

246

HILLVIEW LN S

LORETTO ST

235

130

120

110

100

140

MEADOW DR

150

125

115

105

160

165

215

170

185

205

215

HILLVIEW LN S

180

190

200

210

220

Placement of Sand, Gravel, and Draintile
